

# **Smithtown Central School District**

**Athletic Field Renovations – HS West**

**Fieldhouse Additions – HS East & West**

**Fire Alarm Reconstruction – HS West**

**Project Briefing : April 2023**

**Board of Education Update**

**May 2, 2023**

## Table of Contents

- a. Project Briefing
- b. Progress Photographs

## Project Briefing – May 2, 2022

### **Smithtown Central School District**

#### Work completed in March 2023

#### Smithtown High School West – Athletic Field Renovations

- Spring sports officially underway. All renovated fields are currently being used!

#### Smithtown High School East & West – Field Houses

- **East**


- Finished painting
- Started plumbing fixtures
- Start stucco
- Finished base asphalt, storage area and fencing around storage area
- **UPCOMING WORK:**
- Epoxy floors, final grading/landscaping, finish plumbing fixtures and toilet partitions, septic system control panel

- **West**


- Installed all doors
- Installed epoxy flooring
- Completed all plumbing fixtures
- Installed toilet partitions
- Installed kitchen cabinetry
- Finished asphalt and landscaping
- **UPCOMING WORK:**
- Start and complete punch list items, septic system startup, transformer install, turnover and closeout

#### Smithtown High School West Fire Alarm Reconstruction

- Continue installing devices
- Corrective work on exposed conduit/boxes
- Continue pulling cable between panels
- **UPCOMING WORK:** continue mounting devices and corrective work

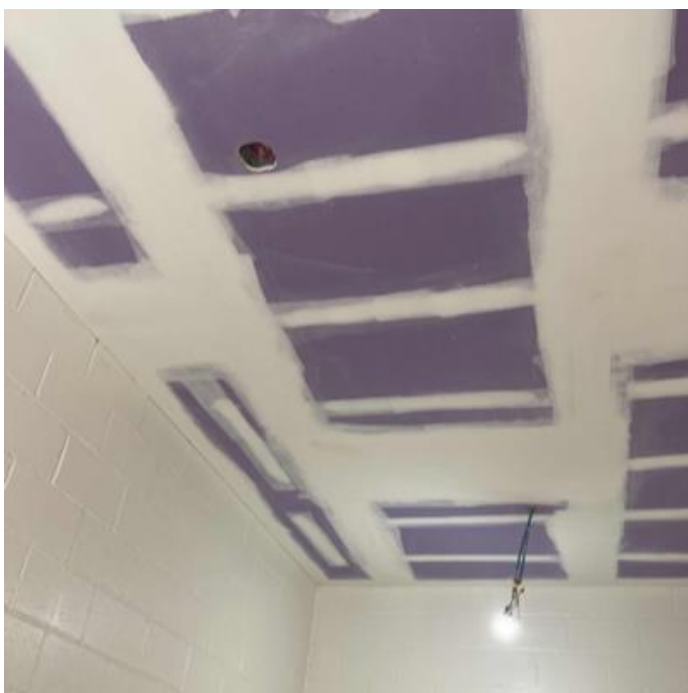

East Field House – Complete densglass in preparation for stucco, tape and sand, storage and septic area fencing

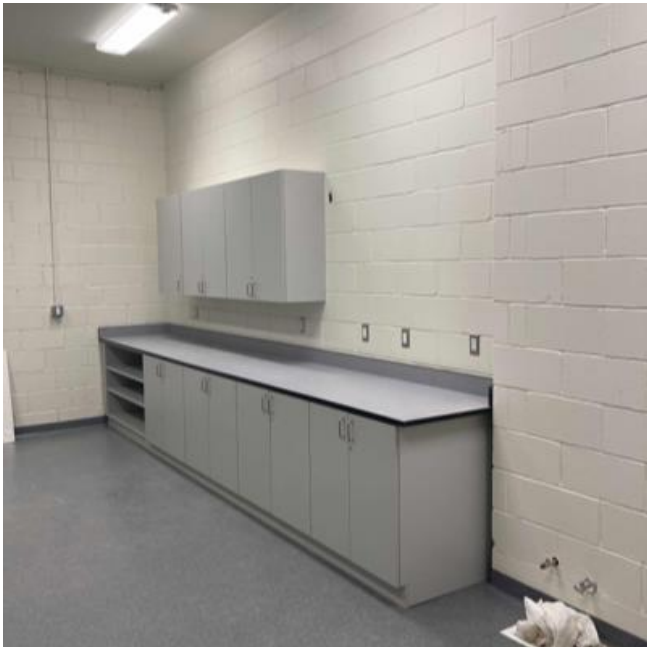

West Field House – Installed all doors, landscape/pave, install kitchen cabinets, install toilet accessories



West Fire Alarm – Continue piping and boxes in gym, loop testing for ground faults
