

# **Smithtown Central School District**

**Athletic Field Renovations – HS West**

**Fieldhouse Additions – HS East**

**Project Briefing : Aug. 2022 – Dec. 2022**

**Board of Education Update**

**December 6, 2022**

## Table of Contents

- a. Project Briefing
- b. Progress Photographs

## Project Briefing – December 6, 2022 Smithtown Central School District

### Work completed in the months of August 2022 thru December 2022

#### Smithtown High School West – Athletic Field Renovations Varsity Softball Field & Varsity Baseball Field

- Demolition of grub and topsoil was completed at the infield
- Existing fencing and backstop was removed
- Upon establishing final subgrade of infield, compaction was completed
- Perimeter perforated corrugated drainage piping installed in basins pitched to new buried storm drywells.
- Drainage felt skin installed at infield and flat pipe drainage system installed throughout infield. Flat piping pitched to perimeter corrugated piping.
- Gravel fines installed to conceal drainage piping and synthetic turf installed.

#### Stadium Field

- Removal of synthetic turf was completed.
- Fine grading and install of additional fine gravel, where required, was completed.
- Awaiting installation of new synthetic turf, scheduled for this week.

**Project Briefing – December 6, 2022**  
**Smithtown Central School District**

**Work completed in the month of December 2022**


**Smithtown High School East – Addition to Field house**

- Security construction chain link fencing installed to define and isolate construction zone.
- Demolition of existing concrete walkways and tree completed at footprint of addition.
- Excavation completed for new footings and foundation walls.
- Footings were formed and poured. Independent testing agency on site to perform required inspections including compaction and rebar testing as well as concrete testing.



Security fencing erected and site demolition commenced at the existing Fieldhouse at HS East.



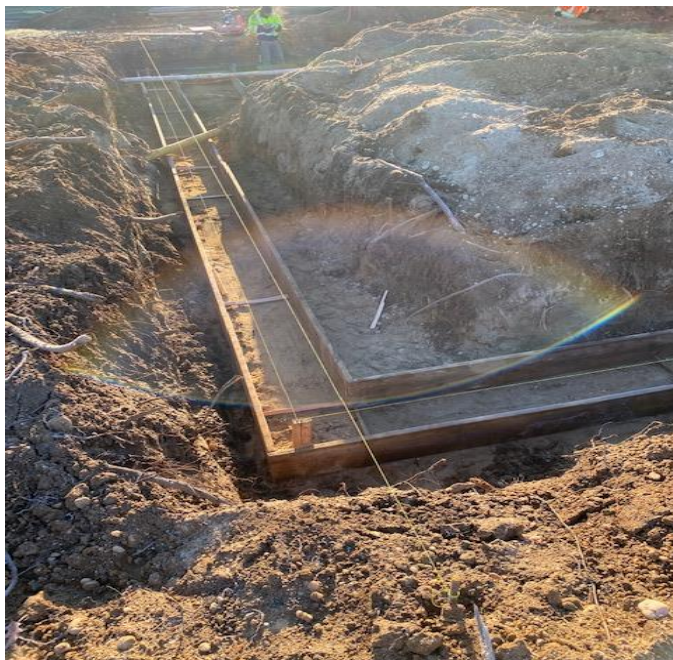

Excavation for the Fieldhouse addition commenced at High School East. Footings are formed and awaiting concrete pour.





Demolition of Varsity Softball & Baseball Fields including removal of topsoil and realignment of baseball field.





Upon removal of topsoil, subgrade elevations established and infields compacted.





Storm drywell systems installed in foul territory outside field of play to collect storm water at softball field and baseball fields.






Corrugated drainage piping installed to at perimeters of softball and baseball fields. Piping to be pitched to drywells.





Upon establishing subgrade, gravel fines installed over flat pipe drainage system. Awaiting synthetic turf install.



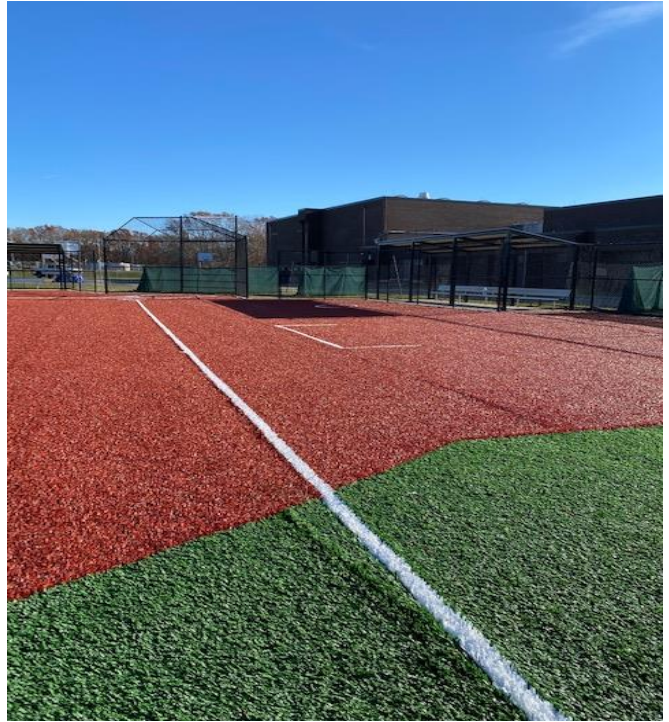

Synthetic turf installed at softball infield. Smithtown West logo installed behind pitchers mound.





Removal of existing synthetic turf completed at stadium field. Additional gravel fines installed as required.
