

Smithtown Central School District

Monthly Project Briefing – July 2024

Board of Education Update June 31,2024 2021 Bond Issue Phase 1 2021 Bond Issue Phase 2



Table of Contents

- a. Project Briefing
- b. Progress Photographs



Project Briefing – July 31, 2024 Smithtown Central School District

Interior Door Replacement Districtwide

Contractor is currently installing doors and hardware at High School West <u>Fire Alarm Reconstruction Districtwide</u>

Electrical contractor is onsite at St James Elementary School installing rough wiring and devices

Unit Ventilation project at High School East (Phase 2)

The Unit Ventilators for classrooms have arrived and are currently being installed, the FAC room is framed and roughed, new ceiling grid has been installed at the corridors and MEP rough is underway. Demolition has commenced at the Auditorium.

UV installation at St James Elementary School

The Unit Ventilators are installed at Classrooms and final patchwork is taking place <u>UV installation at Smithtown Elementary School (Phase 2)</u>


The Unit Ventilators are installed, the casework installation at the North wing has commenced and work ion the boiler has begun.


UV installation at Great Hollow Middle School (Phase 2)

The Guidance area renovation is approx. 90% complete. All renovated bathrooms are framed and receiving gypsum wallboard. Floor preparation in the Science Classrooms has begun, and the locker room demolition and MEP rough is 80% complete






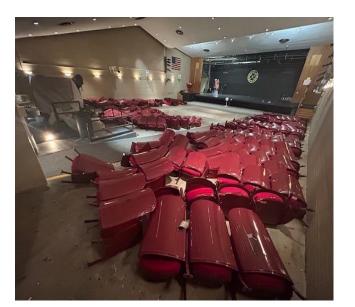

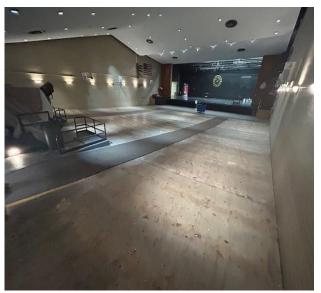

High School East Corridor new ceiling work started, the Auditorium has been demoed and MEP rough has kicked off



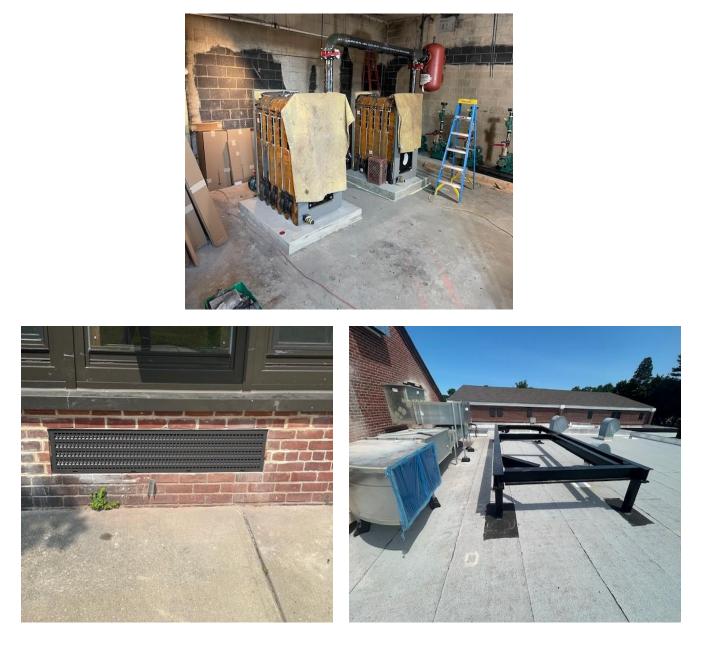


Smithtown Elementary School boiler room started, New exterior fresh air venting installed and roof dunnage to support the new RTU is complete





St James Elementary School Unit Ventilation project the hallway new ceilings installed, the classroom Unit ventilators are installed and the exterior units are being installed and tested



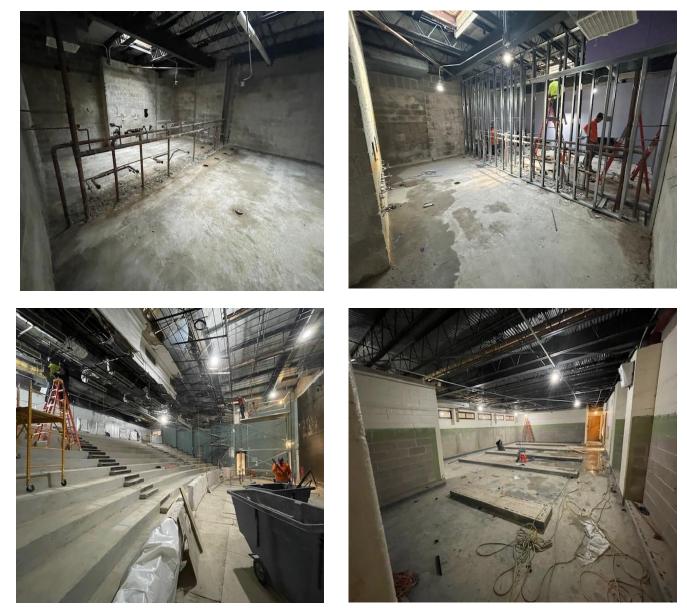

Great Hollow Middle School Unit Ventilation project- Bathroom demo is complete, the Auditorium Demo started and the locker rooms are being roughed in
