

Smithtown Central School District

Monthly Project Briefing – June 2024

Board of Education Update

June 30,2024

2021 Bond Issue Phase 1

2021 Bond Issue Phase 2

Table of Contents

- a. Project Briefing
- b. Progress Photographs

Project Briefing – June 30, 2024 **Smithtown Central School District**

Interior Door Replacement Districtwide

Contractor is currently installing doors and hardware in all elementary school locations, Accomsett Middle School, Nesaquake Middle School and Great Hollow Middle School

Fire Alarm Reconstruction Districtwide

Electrical contractor is onsite at St James Elementary School installing rough wiring and devices

Unit Ventilation project at High School East (Phase 2)

The Electrician has installed a portion of electrical feeds and currently temping off areas of demolition, the Mechanical Contractor has commenced on UV demolition in classrooms, and the General Contractor has commenced and is currently working on corridor ceilings and FACS room demolition

UV installation at St James Elementary School

The Mechanical demolition has begun in boiler area, the Electrical contractor continues with rough installation, and General Contractor has mobilized and started ceiling demolition.

UV installation at Smithtown Elementary School (Phase 2)

The Plumbing contractor performed demolition work, the Mechanical contractor has commenced with demolition, wall layout and louver installation, and the General contractor mobilized and continues with classroom demolition

UV installation at Great Hollow Middle School (Phase 2)

Electrical contractor has commenced and started to install conduits to all locations throughout building. Mechanical contractor has commenced and installed copper runs to new Guidance area along with roof ductwork installation, and the General contractor mobilized and into demolition work




High School East Conduit installation for new Unit Ventilation project conduits and pull box installations



New district wide door Installation district wide in Elementary and Middle schools



Smithtown Elementary School boiler room demolition, new UV louver installation and new framing and drywall behind where UV's will be installed in classrooms

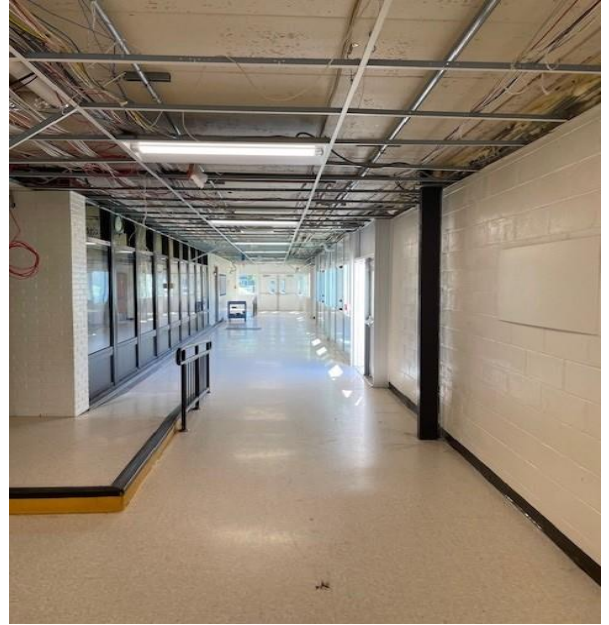

St James Elementary School Unit Ventilation project demolition in corridors and new electrical feeds from common room into boiler room



Great Hollow Middle School Unit Ventilation project- Ductwork installation on roof and Guidance Area Wall Pack installation are ongoing along with Bathroom demolition
