

Smithtown Central School District

**Accompsett Middle School – Various
Interior & Exterior Alterations**

**Various Interior Alterations to Mt Pleasant
ES, Tackan ES & St James ES**

**Board of Education Update
September 24,2026**

Table of Contents

- a. Project Briefing- Accomsett MS
- b. Progress Photographs- Accomsett MS
- c. Project Briefing- Mt Pleasant, Tackan & St James ES's
- d. Progress Photographs- Mt Pleasant, Tackan & St James ES's

Project Briefing – September 24, 2026 **Smithtown Central School District**


Work completed in the months of August & September 2026

Accompsett Middle School



- Completed installation of thru wall flashing at Gymnasium brick veneer at weep holes. Completed removal of damaged brick veneer at existing chimney and installed new replacement brick.
- Alteration of existing Auditorium continued. Installation of new gypsum wallboard soffits and fascia's above locations of proposed hanging clouds commenced.
- Science Room alterations continued as slab floors were leveled and flash patched to accept new LVT flooring. LVT flooring and vinyl base were completed. Installation of new science room casework, countertops & related plumbing fixtures was completed as well as installation of all new loose furniture throughout the science rooms.
- Faculty & student toilet rooms construction was completed. All floor and wall tile was completed and grouted. All lighting and plumbing fixtures were installed at all toilet rooms. All epoxy flooring systems were completed as well.



Science Room concrete slabs are leveled and flash patched in preparation for LVT installation. .

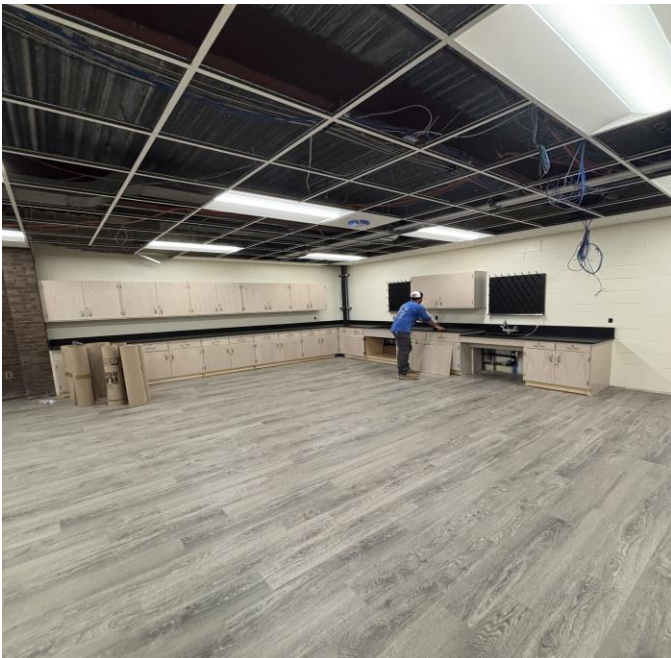



LVT flooring installed at Science Rooms.

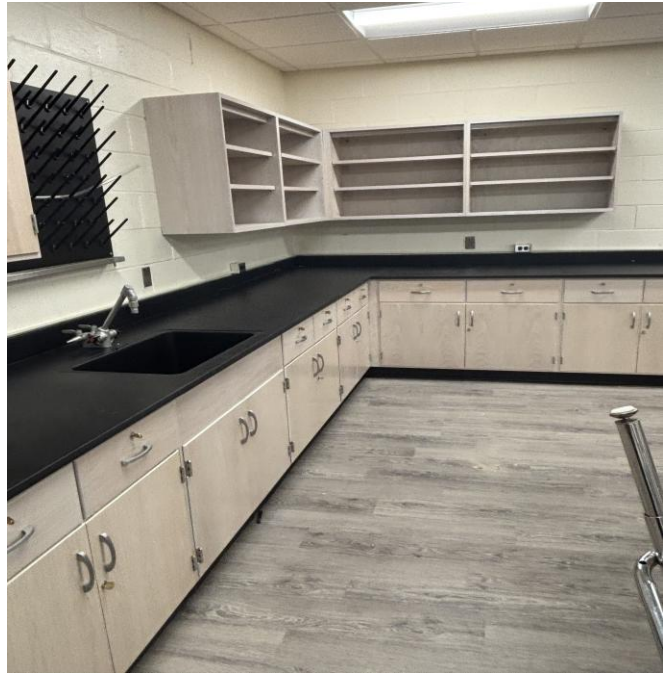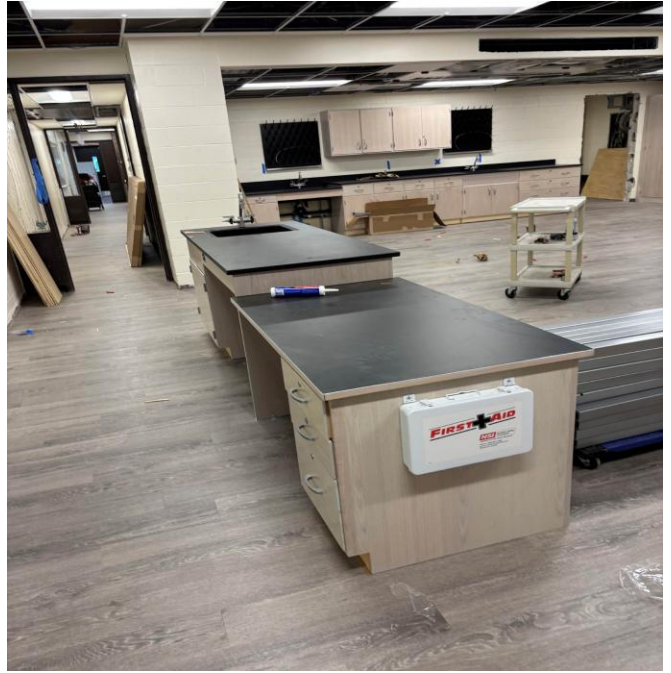

New casework and countertops installed at science rooms.



Plumbing fixtures and toilet accessories installed at toilet rooms.

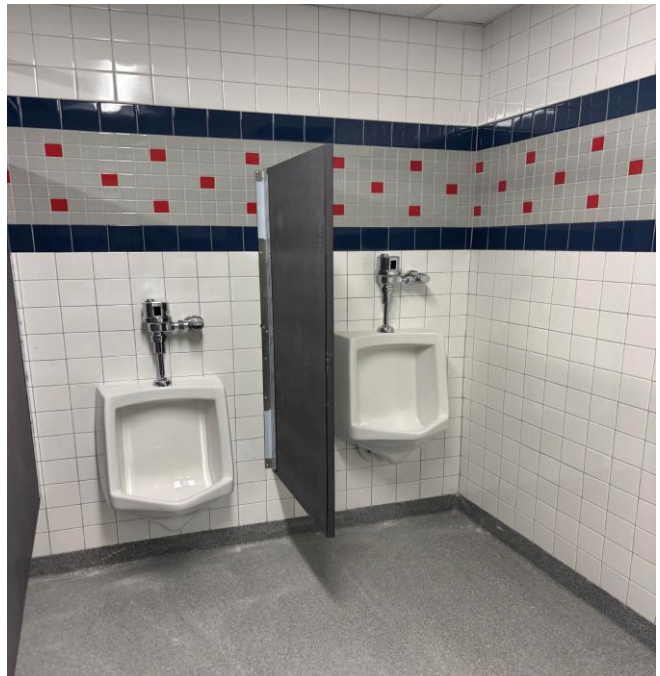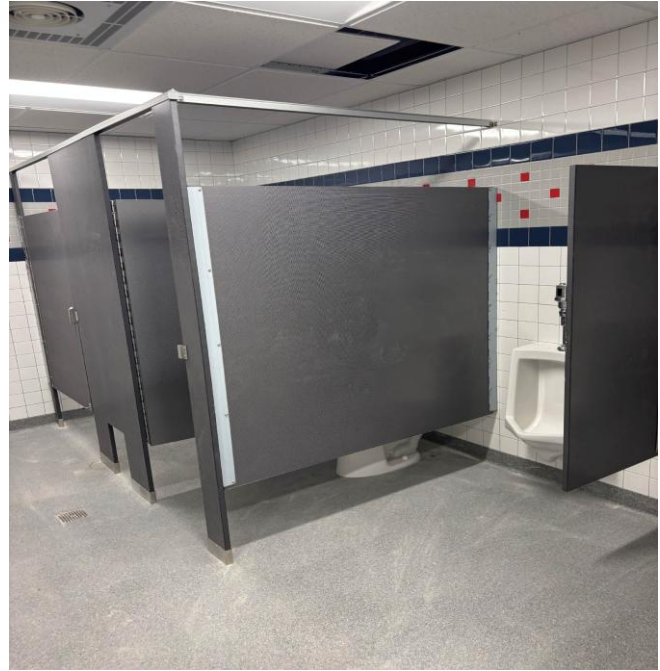

Toilet partitions installed at toilet rooms.

Project Briefing – September 24,2026 **Smithtown Central School District**

Work completed in the months of August & Sept. 2026 **Mt Pleasant ES**

- All toilet rooms walls received epoxy primer and epoxy finish system.
- Slab floors received sub base and epoxy self leveling and prime coat. Epoxy floors completed including installation of floor drains and cleanouts where required.
- New acoustical ceilings and light fixtures installed at toilet rooms.
- Plumbing fixtures, toilet accessories and temporary toilet partitions installed at toilet rooms.
- HC hollow metal door frame installed.

Tackan ES

- All toilet rooms walls received epoxy primer and epoxy finish system.
- Slab floors received sub base and epoxy self leveling and prime coat. Epoxy floors completed including installation of floor drains and cleanouts where required.
- New acoustical ceilings and light fixtures installed at toilet rooms.
- Plumbing fixtures, toilet accessories and temporary toilet partitions installed at toilet rooms.
- HC hollow metal door frame installed
- New gypsum wallboard kneewalls completed in classrooms.

Project Briefing – September 24,2026 **Smithtown Central School District**

Work completed in the months of August & Sept. 2026 **(continued)**

Tackan ES



- **Installation of new PTAC and unit ventilator completed in Classrooms 17 & 35**

St James ES

- * **All toilet room walls received epoxy primer and epoxy finish system.**
- **Slab floors received sub base and epoxy self leveling and prime coat. Epoxy floors completed including installation of floor drains and cleanouts where required.**
- **New acoustical ceilings and light fixtures installed at toilet rooms.**
- **Plumbing fixtures, toilet accessories and temporary toilet partitions installed at toilet rooms.**
- **HC hollow metal door frames installed including new steel lintels.**
- **Window pockets consisting of metal studs and gypsum wallboard completed at (4) toilet rooms.**



Application of epoxy wall primer completed at Mt Pleasant ES toilet rooms.

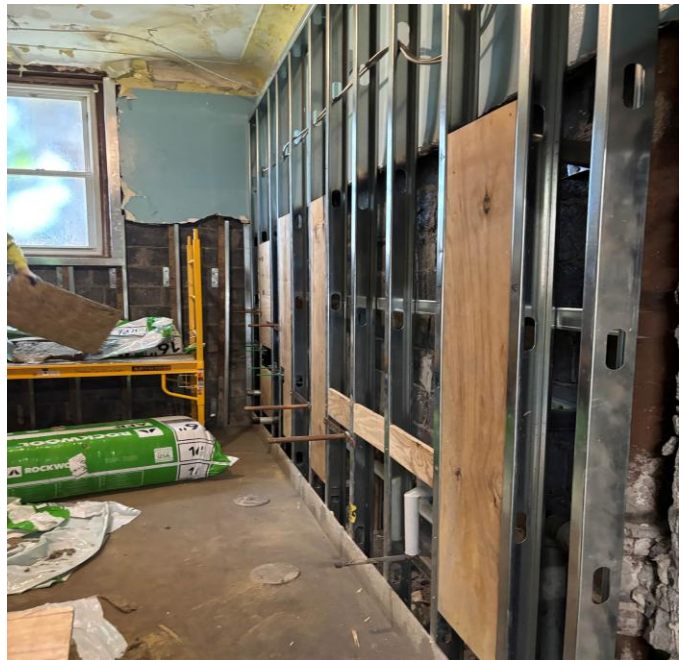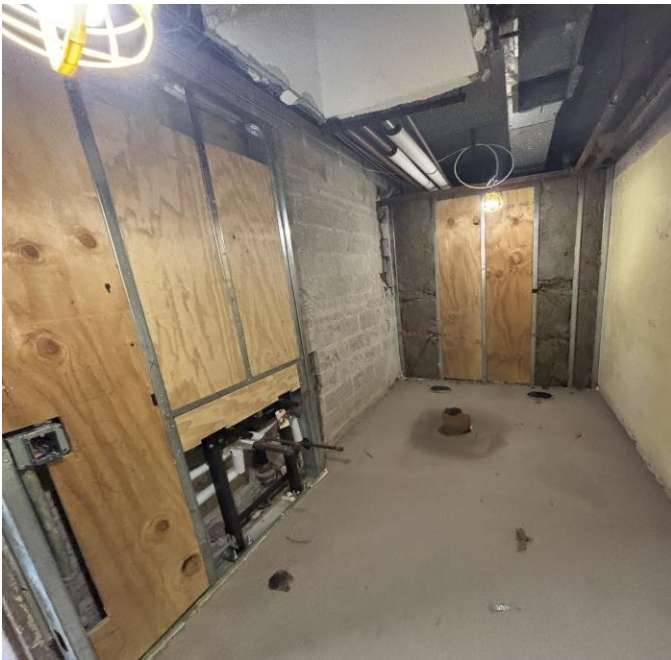

Installation of plywood sheathing at newly framed metal stud walls at St James ES toilet rooms.



Epoxy wall finish applied to walls at Mt Pleasant ES toilet rooms.



Epoxy self leveling and sub base completed. Epoxy floor primer installed at toilet rooms at Mt Pleasant ES..



Epoxy floors and walls completed. Plumbing fixtures and toilet accessories and toilet partitions installed at St James ES.
