

Smithtown Central School District

Athletic Field Renovations – HS West

Fieldhouse Additions – HS East & West

Fire Alarm Reconstruction – HS West

Project Briefing : March 2023

Board of Education Update

April 7, 2023

Table of Contents

- a. Project Briefing
- b. Progress Photographs

Project Briefing – April 7, 2022 **Smithtown Central School District**

Work completed in March 2023

Smithtown High School West – Athletic Field Renovations

- Spring sports officially underway. All renovated fields are now being used!

Smithtown High School East & West – Field Houses


- **East**
 - Complete roofing and siding. Building now watertight.
 - Carpenters continue bracing and misc. support for trusses.
 - Masons prepared block walls for paint
 - Roll up gates installed in concession area
 - UPCOMING WORK:
 - Paint, asphalt driveway, drywall, plumbing fixtures
- **West**
 - Finished painting all surfaces
 - Start installing plumbing fixtures
 - Site cleanup and prep for asphalt
 - Finished installing light fixtures
 - Turnover shed and athletic storage to school for use
 - UPCOMING WORK:
 - Epoxy floors, complete all plumbing fixtures, asphalt

Smithtown High School West Fire Alarm Reconstruction


- Start and continue installing devices
- Mount all fire alarm panels
- UPCOMING WORK: continue mounting devices



East Field House – Complete roofing and siding, install roll up gates, grade and prep driveway for asphalt

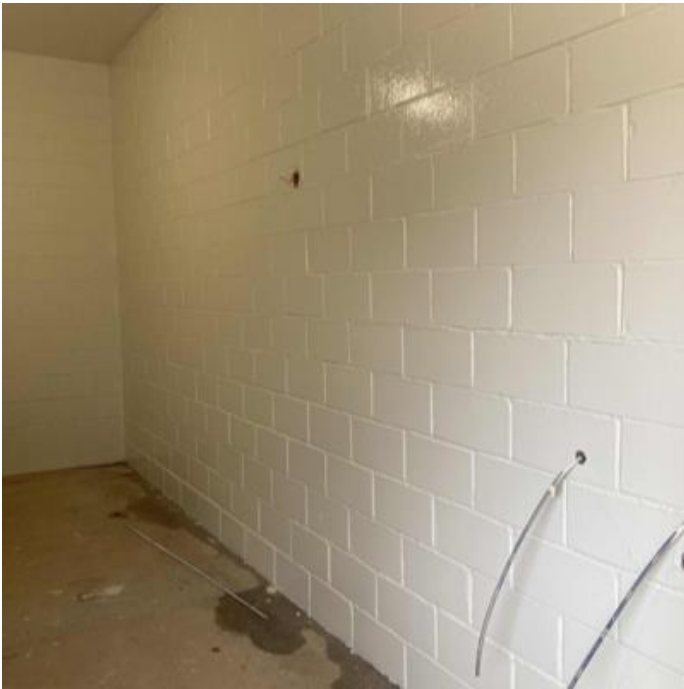

West Field House – Continue and finish painting, install plumbing fixtures, stucco underside of canopy, light fixtures

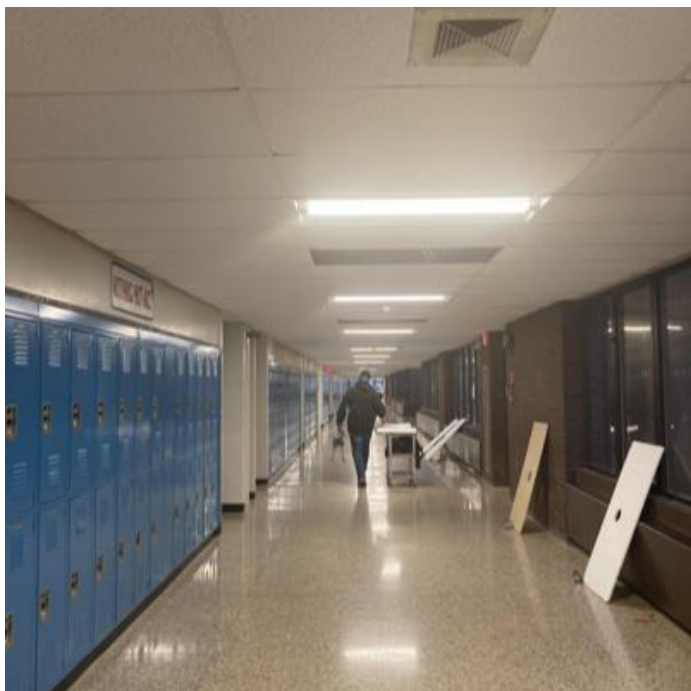

West Fire Alarm – Start and continue installing devices, mount all fire alarm panels
