

Smithtown Central School District

Monthly Project Briefing – September 2023

Board of Education Update

**September 30th, 2023
2021 Bond Issue Phase 1**

Table of Contents

- a. Project Briefing
- b. Progress Photographs

Project Briefing – September 30, 2023
Smithtown Central School District

Exterior Door and Window replacement St. James Elementary School

Project is near completion as ready for punch list .

Exterior Door and Window replacement Smithtown Elementary school

.Project is 95% complete and ready for punch list

Exterior Door and Window replacement Smithtown West HS

Window installation is complete and door installation was started last week of September, remainder of the blind installation is to be complete in October

New Roof Reconstruction at Smithtown HS west

New coating system was installed and contractor is working on completion of the punch list items issued- completion expected early October

Interior Door replacement District wide

Contractor is currently installing doors and hardware in St James Elementary school, Smithtown Elementary school, and Accomsett elementary school

Fire Alarm Reconstruction District wide

Multiple school locations are getting added devices- Contractors are currently in a couple locations and testing

Masonry reconstruction at St James Elementary

Contractor is complete and working on punchlist that was issued

Masonry reconstruction at Smithtown HS west


Contractor is complete with contract work and working on punchlist that was issued

Field improvements at Smithtown HS east

Contractor has scheduled the track to be line striped in November once the seasonal sports are complete and working on completing the concrete pad for bleachers on the baseball field

Field Improvements at Smithtown HS West

Contractor has scheduled the track to be line striped in November once the seasonal sports are complete

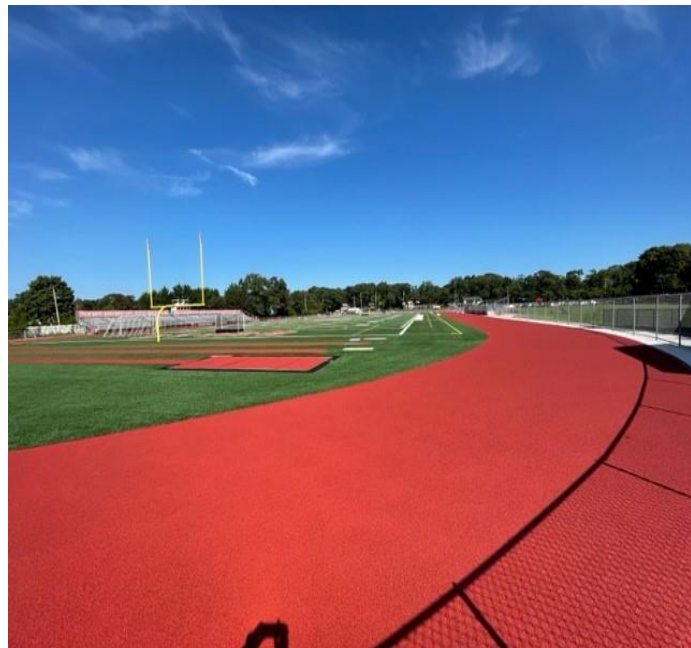

Smithtown High School East new track installation




1



Smithtown High School East Baseball and Softball field installation



New field turf at Smithtown High School East football field

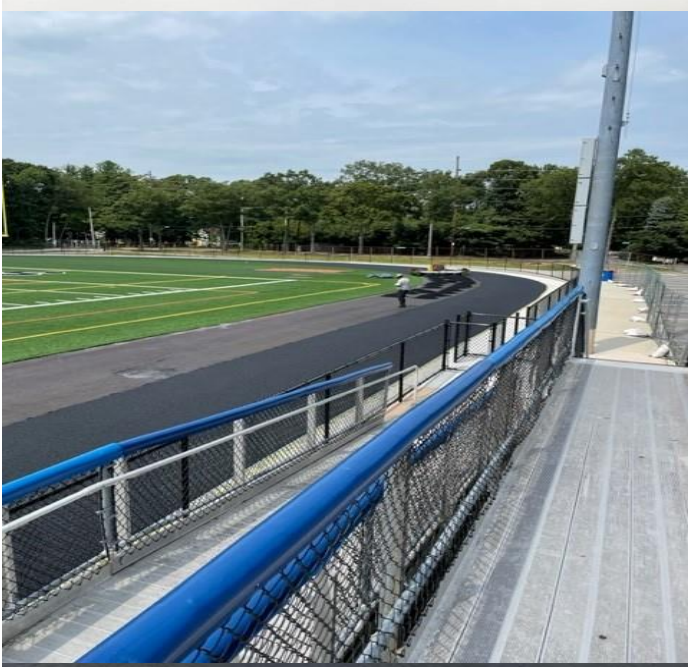

New track installation at Smithtown High School West



District Wide new Door installation is underway in three locations- Accomsett Elementary School, St James Elementary School and Smithtown Elementary School



District wide Fire Alarm Upgrades in progress- currently in Dogwood Elementary school (panel above), High School West, Accomsett Middle school and Elementary Schools, Smithtown Elementary School, Tackan Elementary School, Mills Pond Elementary School, Mt Pleasant Elementary School



Smithtown High School West new roof Coating is in punch list phase currently



Smithtown High School West New window install and Brick repointing along with misc. lintel replacement above various windows.



St James Elementary School New Window installation along with repointing around the main Gym and new walkway to new door in corridor behind the multipurpose room
