Smithtown Central School District

Accompsett Middle School – Various Interior & Exterior Alterations

Board of Education Update

November 12, 2026

Table of Contents

a. Project Briefing- Accompsett MS
b. Progress Photographs- Accompsett MS

TRITON
CONSTRUCTION COMPANY

Project Briefing – November 12, 2026

Smithtown Central School District


Work completed in the month of October / November (partial) 2026


Accompsett Middle School (Auditorium)

- All new hung gypsum wallboard received tape & spackle and new paint finish.
- Scaffolding system erected at the left and right of the Auditorium allowing all contractors to access and install all electrical, mechanical and GC related material and equipment.
- All installations above the center Auditorium seating location to be accessed by mechanical scissor lifts.
- All above existing surfaces (above proposed cloud locations) were sprayed matt black finish.
- All mechanical ductwork, trunks & branches, were installed above proposed cloud locations tight to existing structural steel and decking above.
- All electrical roughing and boxes for new pendent hung light fixtures installed, including wire pulled.
- Installation of all hanging equipment (threaded rod & kindorf and chains) completed above.
- Threaded rod and kindorf installed for cloud support below ductwork.
- Modifications to existing stage front and enlargement to stage completed.
- New pendent hung light fixtures installed.
-

*



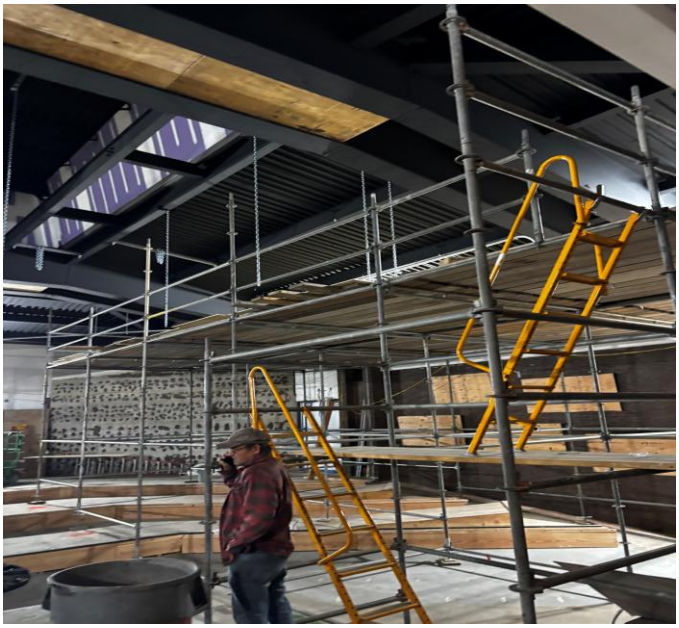

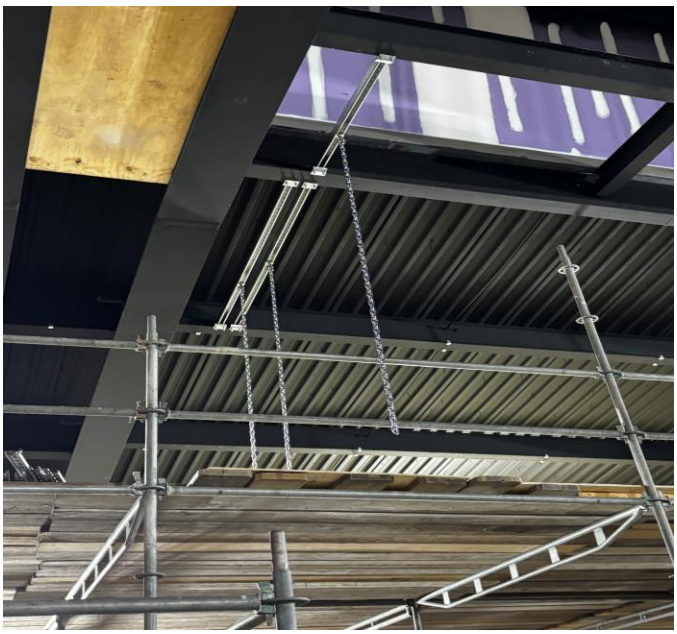



Installation of scaffolding, threaded rod, kindorf and chains commenced at Auditorium.

TRITON
CONSTRUCTION COMPANY










Outline of proposed clouds layed out on floor, to be transposed above with a laser to ensure exact locations.

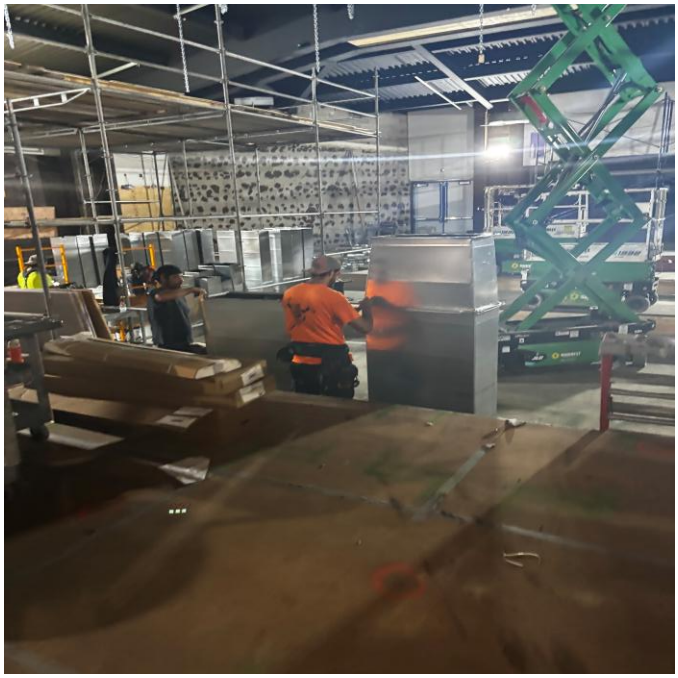







HVAC ductwork fabricated and in process of being hung. All trunks and branches completed.










All existing surfaces above clouds including structural steel, metal decking and conduits sprayed matt black..



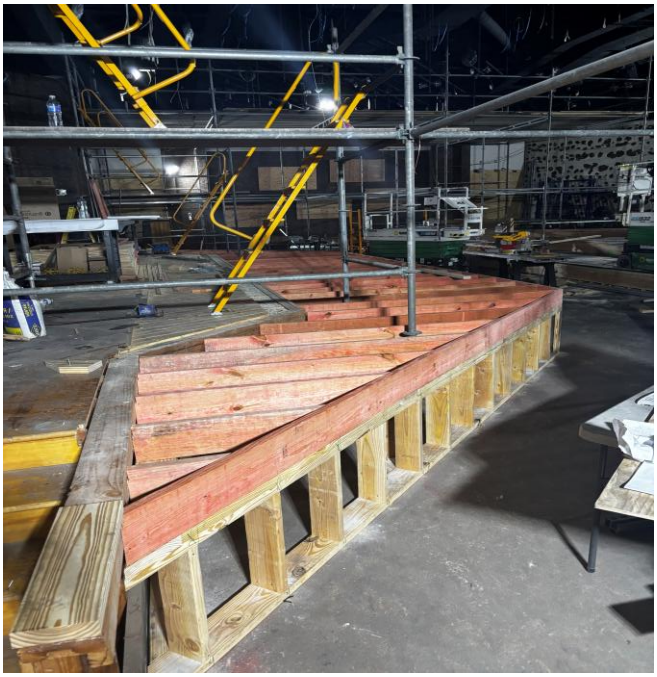





Existing stagefront modified and enlarged.









New pendent hung light fixtures installed from steel and deck above. Positioned to fall between hung clouds.
